

**GOVERNMENT OF PUERTO RICO
PUERTO RICO PUBLIC SERVICE REGULATORY BOARD
PUERTO RICO ENERGY BUREAU**

NEPR

Received:

Feb 28, 2025

8:02 PM

IN RE:

REVIEW OF THE PUERTO RICO
ELECTRIC POWER AUTHORITY'S 10-
YEAR INFRASTRUCTURE PLAN-
DECEMBER 2020

CASE NO. NEPR-MI-2021-0002

**SUBJECT: Informative Motion on the Status of
SOW: 4 x 25 MW BESS Interconnections at
LUMA 38kV System**

**INFORMATIVE MOTION ON THE STATUS OF SOW: 4 X 25 MW BESS
INTERCONNECTIONS AT LUMA 38KV SYSTEM**

TO THE PUERTO RICO ENERGY BUREAU:

COME NOW LUMA Energy, LLC, and LUMA Energy ServCo, LLC, (jointly referred to as “LUMA”), through the undersigned legal counsel and respectfully submit the following:

1. On March 26, 2021, this Honorable Puerto Rico Energy Bureau (“Energy Bureau”) issued a Resolution and Order in the instant proceeding, ordering, in pertinent part, that the Puerto Rico Electric Power Authority (“PREPA”) submit to the Energy Bureau the specific projects to be funded with Federal Emergency Management Agency (“FEMA”) funds or any other federal funds at least thirty (30) calendar days prior to submitting these projects to the Puerto Rico Central Office for Recovery, Reconstruction and Resiliency (“COR3”), FEMA or any other federal agency (“March 26th Order”). It also directed PREPA to continue reporting to the Energy Bureau and FEMA within the next five years, the progress of all ongoing efforts related to the approval of the submitted projects not yet approved by the Energy Bureau. This Energy Bureau thereafter determined this directive applied to PREPA and LUMA. *See* Resolution and Order of August 20, 2021.

2. On August 25, 2023, LUMA filed a *Motion Submitting One Scope of Work, Request for Confidentiality, and Supporting Memorandum of Law*. Therein, LUMA submitted the scope of

work (“SOW”) for the “4 x 25 MW BESS Interconnections at LUMA 38kV System” transmission and distribution project (“T&D Project”), for the Energy Bureau’s review and approval before submitting it to COR3 and FEMA (“August 25th Motion”).

3. On August 30, 2023, the Energy Bureau entered a Resolution and Order in which it approved the “4 x 25 MW BESS Interconnections at LUMA 38kV System” T&D Project SOW. It determined that this project was necessary to improve the system’s reliability (“August 30th Order”).

4. Then, on January 3, 2025, the Energy Bureau entered a Resolution and Order in which it ordered LUMA “to inform, on or before January 9, 2025, the status of the approval process, the actual contracted cost to construct, and the status of the project” (“January 3rd Order”). See January 3rd Order, p.2.

5. On January 9, 2025, LUMA filed its *Informative Motion on the Status of SOW: 4 x 25 MW BESS Interconnections at LUMA 38kV System* to comply with the January 3rd Order.

6. On January 14, 2025, the Energy Bureau issued a Resolution and Order whereby it ordered LUMA to file a status report of the project until its June 2025 completion date (“January 14th Order”). See January 14th Order at 2. The status report should include:

- i) The locations of the twenty (20) sites studied;
- ii) The final four selected sites;
- iii) The cost to complete the studies of the twenty sites.
- iv) Indicate the funds utilized to pay for these studies and the amount spent to date.
- v) The reimbursement status of these funds, or if they were advanced by FEMA
- vi) The DSOW presented to FEMA and COR3;
- vii) The ROT and LUMA responses to such ROT requested by FEMA and COR3;
- viii) The FAAS number for the project; and
- ix) An updated cost estimate based on the DSOW.

See Id.

7. In compliance with the January 14th Order, LUMA hereby submits its monthly status report as *Exhibit 1* to this motion.

WHEREFORE, LUMA respectfully requests that the Energy Bureau **take notice** of the aforementioned, **accept** Exhibit 1 submitted herein, and **deem** LUMA in compliance with the January 14th Order.

RESPECTFULLY SUBMITTED.

We hereby certify that we filed this motion using the electronic filing system of this Energy Bureau. We will send an electronic copy of this motion to counsel for PREPA Alexis Rivera, arivera@gmlex.net, and to Genera PR LLC, through its counsel of record, Jorge Fernández-Reboredo, jfr@sbglaw.com and Alejandro López Rodríguez, alopez@sbglaw.com.

In San Juan, Puerto Rico, on this 28th day of February 2025.



DLA Piper (Puerto Rico) LLC
500 Calle de la Tanca, Suite 401
San Juan, PR 00901-1969
Tel. 787-945-9132
Fax 939-697-6102

/s/ *Yahaira De la Rosa Algarín*
Yahaira De la Rosa Algarín
RUA NÚM. 18,061
yahaira.delarosa@us.dlapiper.com

Exhibit 1

4x25 MW BESS Interconnections at LUMA 38 kV System Project Monthly Status Report

February 28, 2025




Contents

Tables & Figures	3
1.0 Introduction	4
2.0 Monthly Status Update	4
2.1 Detailed Scope of Work	4
2.2 Procurement	4
2.3 Design Status	4
2.4 Project Schedule	4
3.0 Project Status	5
3.1 Selected Sites	5
3.2 Reimbursement Status	5
3.3 Requests of Information	5
3.4 FAASt Number	5
3.5 Updated Project Cost	5

Tables & Figures

Table 3-3. FAASt Number 5

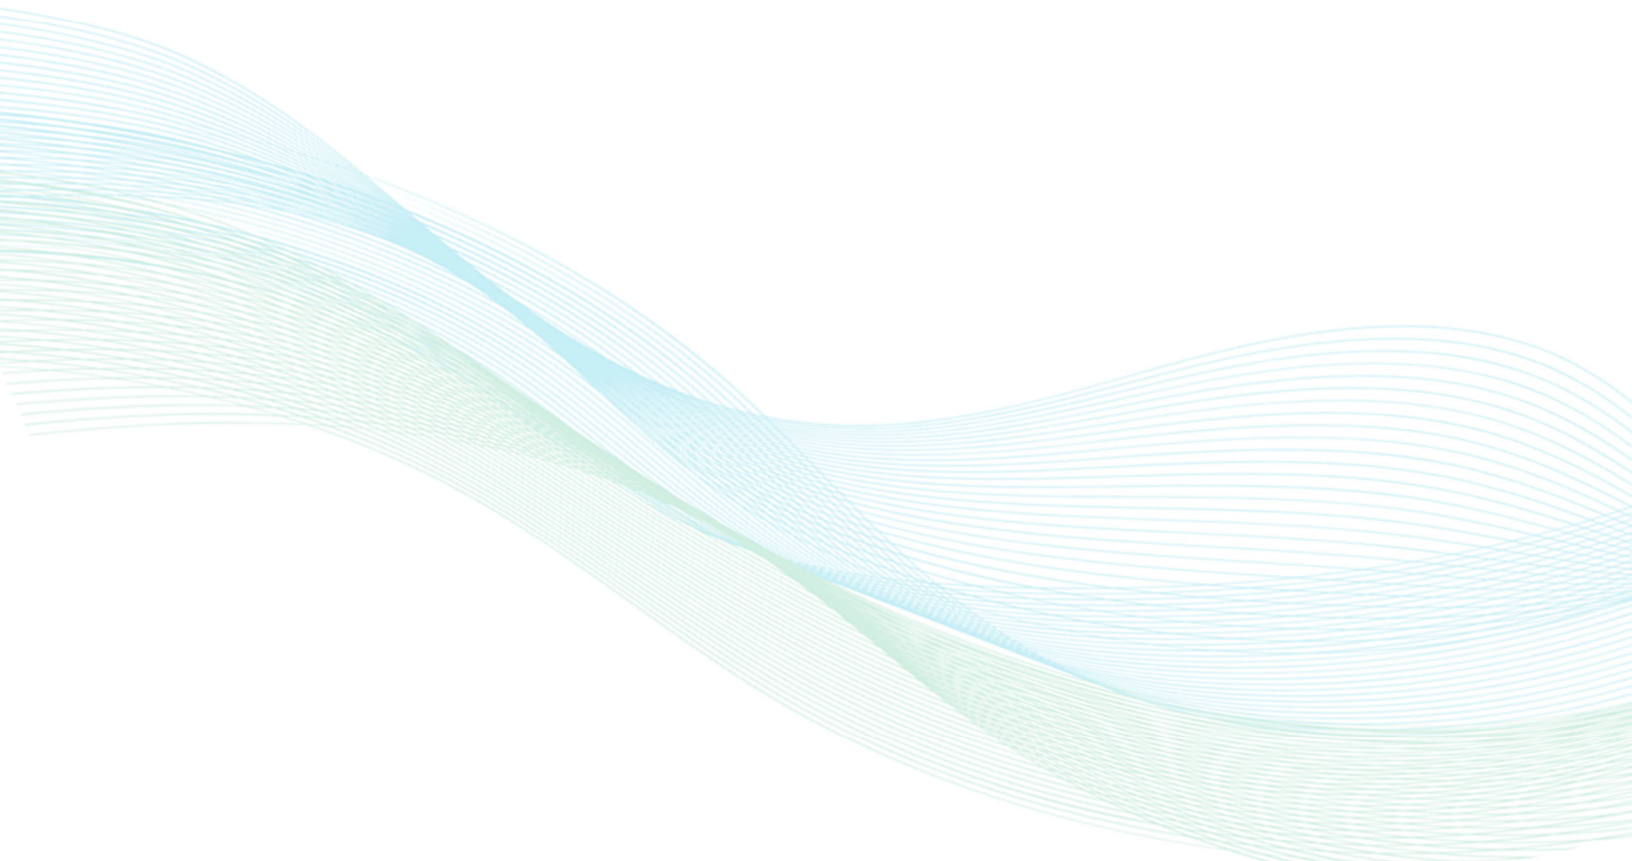

NEPR-MI-2021-0002

1.0 Introduction

In accordance with the Resolution and Order dated January 14, 2025, issued by the Puerto Rico Energy Bureau (PREB) in Case No.: NEPR-MI-2021-0002 *In Re: Review of the Puerto Rico Power Authority's 10-Year Infrastructure Plan – December 2020*, LUMA is required to provide a monthly report regarding the 4x25 MW BESS Interconnections at LUMA 38 kV project. This report focuses on the key activities and progress achieved by LUMA in the past 30 days for the Battery Energy Storage Systems (“BESS” or collectively as the “Project”) approved by the PREB in its Resolution dated August 30, 2023 (“August 30th Resolution”).

2.0 Monthly Status Update

2.1 Detailed Scope of Work

LUMA is in the process of completing the detailed scope of work (DSOW) and expects to submit it in March 2025 to the Central Office for Recovery, Reconstruction and Resiliency (COR3) and the Federal Emergency Management Agency (FEMA).

2.2 Procurement

LUMA has completed drafts for the scopes of procurements for the engineering, procurement, and construction services that will be needed for the execution of the Project. LUMA expects to issue the request for proposal (RFP) in the first quarter (Q1) of fiscal year 2026 (FY26).

2.3 Design Status

The Preliminary Design has been completed. The detailed design will be managed by the selected vendor through a competitive procurement process.

2.4 Project Schedule

LUMA has been studying and pursuing the deployment of BESS to multiple locations as part of the Project. LUMA's high-level schedule for this project includes:

- Submission of DSOWs to FEMA and COR3, March 2025, 12 months for obligation (March 2026)
- Procurement: February 2026
- Construction starts April 2026
- Commissioning: May 2027

A more detailed schedule will be provided once the funds have been obligated by FEMA and COR3. These dates depend on LUMA being able to procure resources, including equipment, at the expected times.

3.0 Project Status

3.1 Selected Sites

LUMA has not yet finalized the sites where it intends to deploy the four BESSs but has determined proposed locations across the general areas where the projects would be sited. Specifically, these are (1) Aguadilla, (2) Barceloneta, (3) Manatí, and (4) San Juan. LUMA will supplement its response as final selections are made and real estate details finalized.

3.2 Reimbursement Status

COR3 will be able to reimburse funds associated with the construction of these projects to LUMA once FEMA and COR3 have approved the construction of the project.

3.3 Requests of Information

LUMA has not received any requests for information (“RFI”) from either FEMA or COR3.

3.4 FAASSt Number

As indicated in Section 3.2 above, LUMA has identified four areas where it intends to site the projects. The FEMA FAASSt numbers for the four BESS projects are:

Table 3-3. FAASSt Number

Project Title	FEMA FAASSt #
FAASSt [4 x 25 MW BESS Interconnections on LUMA System] (Substation)	738671
FAASSt [4 x 25 MW BESS Interconnections Manatí] (Substation)	752972
FAASSt [4 x 25 MW BESS Interconnections Aguadilla TC] (Substation)	750502
FAASSt [4 x 25 MW BESS Interconnections Monacillos TC] (Substation)	750503

3.5 Updated Project Cost

An updated cost estimate based on the DSOW is not available yet. Once the DSOWs are submitted to FEMA and COR3 in March 2025, LUMA will provide the Class 3 cost estimates for the Project.
