

**GOVERNMENT OF PUERTO RICO
PUBLIC SERVICE REGULATORY BOARD
PUERTO RICO ENERGY BUREAU**

NEER

Received:

Apr 9, 2021

10:51 AM

IN RE: THE UNBUNDLING OF THE
ASSETS OF THE PUERTO RICO
ELECTRIC POWER AUTHORITY

CASE NO.:
NEPR-AP-2018-0004

SUBJECT:
Weekly Status Report;
April 9, 2021

**MOTION TO SUBMIT WEEKLY STATUS REPORT FOR
THE WEEK ENDING ON APRIL 9, 2021**

TO THE HONORABLE PUERTO RICO ENERGY BUREAU:

COMES NOW, the Puerto Rico Electric Power Authority (the “Authority”), through its undersigned counsel and, in compliance with the February 5, 2021 Order¹, respectfully submits the *Estimate of Deliverables and Timing of Meeting Regulatory Commitment for an Unbundled Rate Proposal* (the “Weekly Status Report”) dated April 9, 2021. Exhibit A.

The Weekly Status Report summarizes the projected schedule duration, identifies milestones completed, lists and describes major tasks performed, and provides a progress timeline.

WHEREFORE, the Authority respectfully requests the Puerto Rico Energy Bureau of the Public Service Regulatory Board to note the Authority’s compliance with the Order.

RESPECTFULLY SUBMITTED.

In San Juan, Puerto Rico, this 9th day of April 2021.

¹ *Resolution and Order* entered on February 5, 2021 (the “Order”).

Katiuska Bolaños Lugo
kbolanos@diazvaz.law
TSPR 18,888

/s Joannely Marrero Cruz
Joannely Marrero Cruz
jmarrero@diazvaz.law
TSPR 20,014

DÍAZ & VÁZQUEZ LAW FIRM, P.S.C.
290 Jesús T. Piñero Ave.
Oriental Tower, Suite 1105
San Juan, PR 00918
Tel. (787) 395-7133
Fax. (787) 497-9664

CERTIFICATE OF SERVICE

It is hereby certified that, on this same date, I have filed the above motion with the Office of the Clerk of the Energy Bureau using its Electronic Filing System at <https://radicacion.energia.pr.gov/login>, and a courtesy copy of the filing was sent via e-mail to hrivera@oipc.pr.gov, ramonluisnieves@rlnlegal.com; manualgabrielfernandez@gmail.com; ccf@tcm.law.

In San Juan, Puerto Rico, this 9th day of April 2021.

/s Joannely Marrero Cruz

Joannely Marrero Cruz

Exhibit A



Memorandum

To: Puerto Rico Electric Power Authority
From: Guidehouse
Date: April 9, 2021
Re: Puerto Rico Energy Bureau Weekly Status Report, *Estimate of Deliverables and Timing of Meeting Regulatory Commitment for an Unbundled Rate Proposal*

This status report describes work performed in the preceding week, **April 2 – 8, 2021**, on the tasks outlined in the *Estimate of Deliverables and Timing of Meeting Regulatory Commitment for an Unbundled Rate Proposal*, in support of the May 10, 2021 filing deadline established by the Energy Bureau.

Description of Work Performed

- Guidehouse continued wrapping up the last items for the Cost of Service analysis.
- Guidehouse continued rate design activities including:
 - Calculating residual revenue requirements based on current rates / total revenue requirement and marginal revenue calculations
 - Developing other billing determinants for marginal and residual rate design
- Guidehouse continued developing the universal services agreement for wheeling that will support the proposed tariff design, including a first draft and internal review.
- Guidehouse, PREPA and LUMA held a project check-in meeting on April 7.
- Guidehouse began conducting interviews for the Rate Implementation Assessment. Because of scheduling constraints for interviewees, this sub-task will extend an additional one week.


Progress by Task

Task	Description	Estimated Duration ¹	Progress
Data Collection	Gather all relevant cost, planning and load forecast data from PREPA, to include anticipated transmission flows and interconnections.	3 weeks	100%
Data Review	Review data for quality and design proxies where data are insufficient or poor in quality.	3 weeks	100%

¹ Tasks will be performed in parallel.



Task	Description	Estimated Duration ¹	Progress
Cost of Service Study	Conduct marginal cost of service study, which includes reviewing all planned projects and identification of which projects are designed to meet load growth versus infrastructure improvements, lifecycle replacement and grid hardening.	4 weeks	99%
Rate Design	Design wheeling rate based on cost of service study results.	5 weeks	75%
Implementation Assessment	Interview key PREPA personnel responsible for billing, contract management, metering, accounting and other organizations as needed to determine what PREPA's capabilities are to implement and maintain the proposed wheeling rate.	4 weeks	30%
Test Rate	Test wheeling rate against different ESPC demands.	2 weeks	0%
Uniform Wheeling Agreement	Develop a uniform wheeling services agreement and vet with PREPA's legal teams.	4 weeks	30%
Filing Preparation	Prepare regulatory filing, including professional testimony and supporting workpapers.	4 weeks	0%
Filing Review	Review and QC final workpapers and testimony.	2 weeks	0%

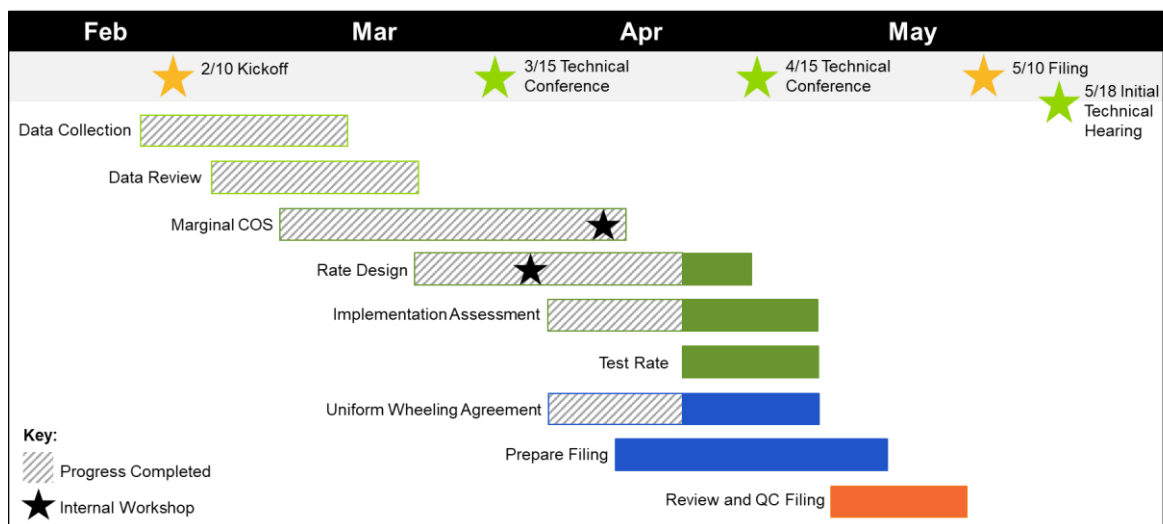

Issue Register

No issues to report at this time.
